
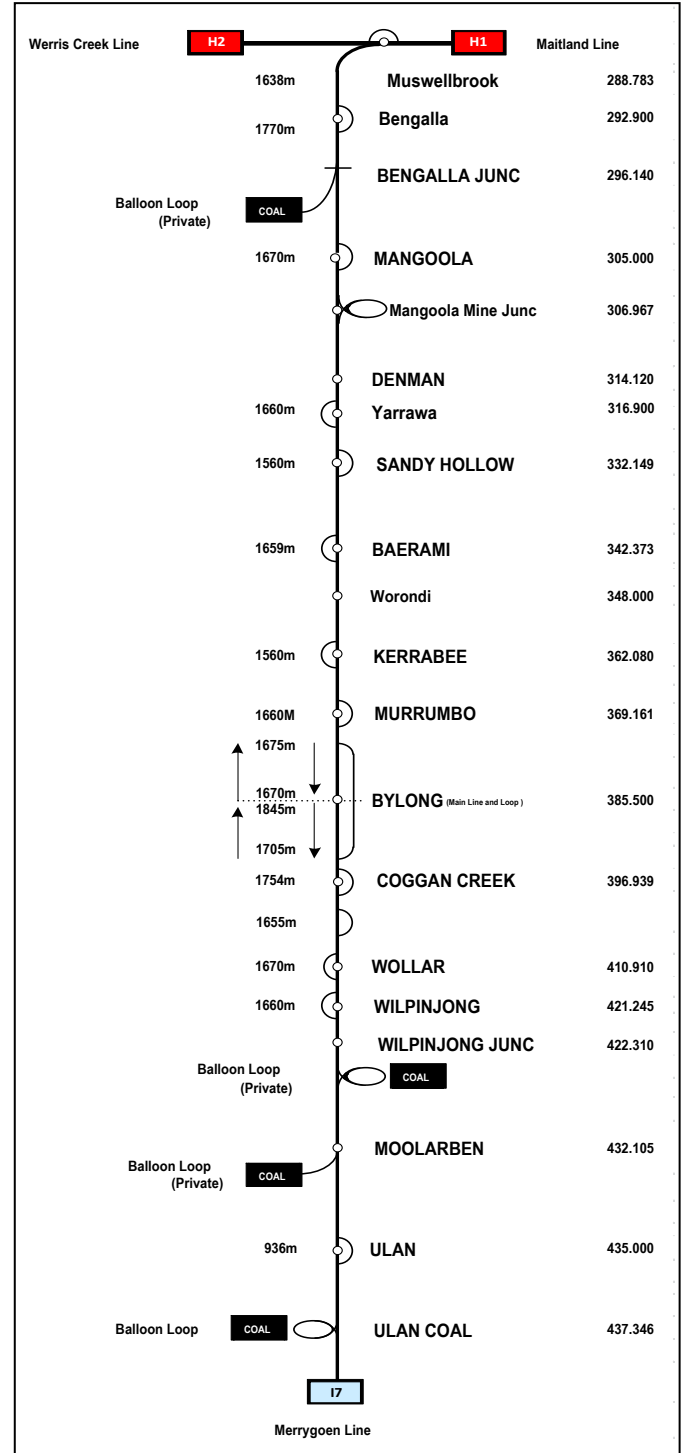


From:

To:

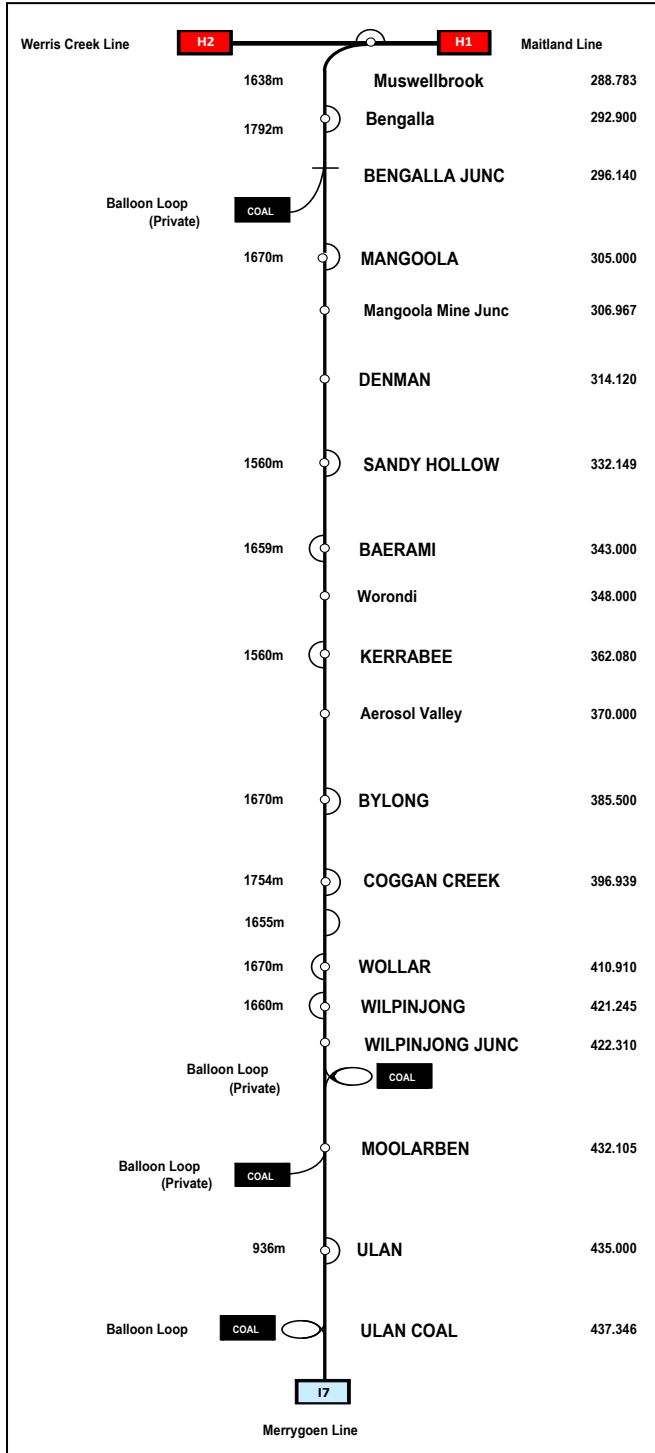

From:

LOCATION	KILOMETRAGE	DOWN		UP	
		Normal	XPT	Normal	XPT
KERRABEE	362.080				
	363.680	75	-	-	-
	366.900	-	-	75	-
	367.002	65	-	-	-
	368.745	-	-	65	-
	369.110	80	-	-	-
	369.150	X80	-	-	-
	369.312	80(OL)		X80(OL)	-
	370.940	X80(OL)	-	80(OL)	-
	371.100	-	-	X80	-
	373.000	-	-	80	-
	373.416	70	-	-	-
	377.000	-	-	70	-
	377.737	60	-	-	-
	379.500	-	-	60	-
	379.811	65	-	-	-
	381.248	-	-	65	-
	381.600	75	-	-	-
	382.269	X55	-	-	-
	382.419	55 (OL)	-	X55 (OL)	-
	384.110	X55 (OL)	-	55 (OL)	-
	384.260	-	-	X55	-
	385.000	-	-	75	-
	385.450	70	-	-	-
	387.000	-	-	70	-
	387.850	115	-	-	-
	390.275	-	-	115	-
	390.695	70	-	-	-
	392.810	-	-	-	70
	393.039	60	-	-	-
393.967	-	-	60	-	
394.400	95	-	-	-	

To:

LOCATION	KILOMETRAGE	DOWN		UP		
		Normal	XPT	Normal	XPT	
KERRABEE	362.080					
	363.680	75	-	-	-	
	366.900	-	-	75	-	
	367.002	65	-	-	-	
	368.745	-	-	65	-	
	369.110	80	-	-	-	
	369.150	X80	-	-	-	
	369.312	80(OL)		X80(OL)	-	
	370.940	X80(OL)	-	80(OL)	-	
	371.100	-	-	X80	-	
	373.000	-	-	80	-	
	373.416	70	-	-	-	
	377.000	-	-	70	-	
	377.737	60	-	-	-	
	379.500	-	-	60	-	
	379.811	65	-	-	-	
	381.248	-	-	65	-	
	381.600	75	-	-	-	
	382.220	X55	-	-	-	
	<i>On loop</i>	382.450	55 (OL)	-	X55 (OL)	-
	<i>On loop</i>	384.110	70	-	55 (OL)	-
		384.260	-	-	X55	-
		385.000	-	-	75	-
		385.450	70	-	-	-
	<i>On loop extension</i>	386.000	X25		70	
		386.085	25		X25	
	<i>On machine siding</i>	386.510	X70		70	
	<i>On loop</i>	386.700			X70	
	<i>On loop extension</i>	387.000	-	-	70	-
		387.850	115	-	-	-
		390.275	-	-	115	-
		390.695	70	-	-	-
		392.810	-	-	-	70
	393.039	60	-	-	-	
	393.967	-	-	60	-	
	394.400	95	-	-	-	

Issued By: Richard Potts
Australian Rail Track Corporation

Approved By: John Furness - Manager Standards (Minor)

NAN Ref (if applicable):
